

ReMCoDS

Retail Market Coordination Design Service

ReMCoWG

25.08.2021

ReMCoWG Agenda

Agenda Item	Presenter	Time
Introduction	Lindsay Sharpe, ReMCoDS	12:30 – 12:35
ReMCoSG Meeting Feedback	Lindsay Sharpe, ReMCoDS	12:35 – 12:45
ReMCoWG Action Items	Lindsay Sharpe, ReMCoDS	12:45 – 12:50
Market Design Update	Lindsay Sharpe, ReMCoDS	12:50 – 13:00
De-harmonisation Update	Lindsay Sharpe, ReMCoDS	13:00 – 13:05
Tibco Hub/EMMA Update	Kris Kennedy, NIE Networks	13:05 – 13:15
Smart Metering Update	Niki Michael, CRU	13:15 – 13:20
ReMCoWG To-Do List Review	Lindsay Sharpe, ReMCoDS	13:20 – 13:25
AOB & Closing	Lindsay Sharpe, ReMCoDS	13:25 – 13:30

All participants are kindly requested to mute their phones when dialled into the forum conference call

Minutes from previous ReMCoWG

For Approval Today:

- Minutes (v1.0) from ReMCoWG 23.06.2021

ReMCoSG Update

- There has been 1 ReMCoSG Meeting since the last ReMCoWG – on 18.08.2021. Next ReMCoSG 17.11.2021.

Item	Summary
ReMCoSG Actions Summary	There are no open ReMCoSG Actions.
NI Supplier Rep Update	Supplier raised 2 items. <ul style="list-style-type: none"> Secure Seamless Solution & Prepayment Solution
ROI Supplier Rep Update	Supplier raised no items. <ul style="list-style-type: none"> Reported that System Separation Project is going well
UR Update	Updates give on: <ul style="list-style-type: none"> System Separation MRC
CRU Update	Update given on: <ul style="list-style-type: none"> Smart PAYG Policy Decision
NIE Networks Update	Updates given on: <ul style="list-style-type: none"> Secure Meters DR Test Internet Services Incident Seamless Solution
ESBN Update	Updates given on: <ul style="list-style-type: none"> v13.00.00 v14.00.00 System Separation
TIBCO HUB/EMMA update	Update on: <ul style="list-style-type: none"> TIBCO EMMA hub
De-harmonisation	Update given by NIE Networks
Brexit	No update

ReMCoWG Action Items

- There are no open actions.



ReMCoDS

Retail Market Coordination Design Service

Co-ordinated Retail Market Design Update

Lindsay Sharpe, ReMCoDS



DR1214 – Interim Metering Responsibilities for Battery Storage

DR1214	Details		
Date Raised	06/08/2021	Date last Approved	
Requesting Organisation	MRSO	Jurisdictional Implementation	ROI
Schema Impacting	N	Jurisdictional Applicability	ROI
Latest Version	V1.0		
Change Summary	<p>In the Retail Market there are currently no policies or mechanism to identify and treat Battery Storage units differently to any other type of generator.</p> <p>Following discussions, EirGrid has agreed, as an interim measure, to act as the Meter Data Provider for Battery Storage Units. EirGrid will poll the DSO connected battery storage sites and provide the import and export data to SEMO in a single data stream under a Generator Unit ID, as required by SEMO.</p>		
Classification	<ul style="list-style-type: none"> • At Today's Meeting; For Classification as RoI Specific 		

Upcoming Outages

ReMCoDS

Retail Market Coordination Design Service

There are no outages scheduled for August/September

<http://rmdservice.com/outages-2021>


Lindsay Sharpe
ReMCoDS



NETWORKS



ReMCoWG Update

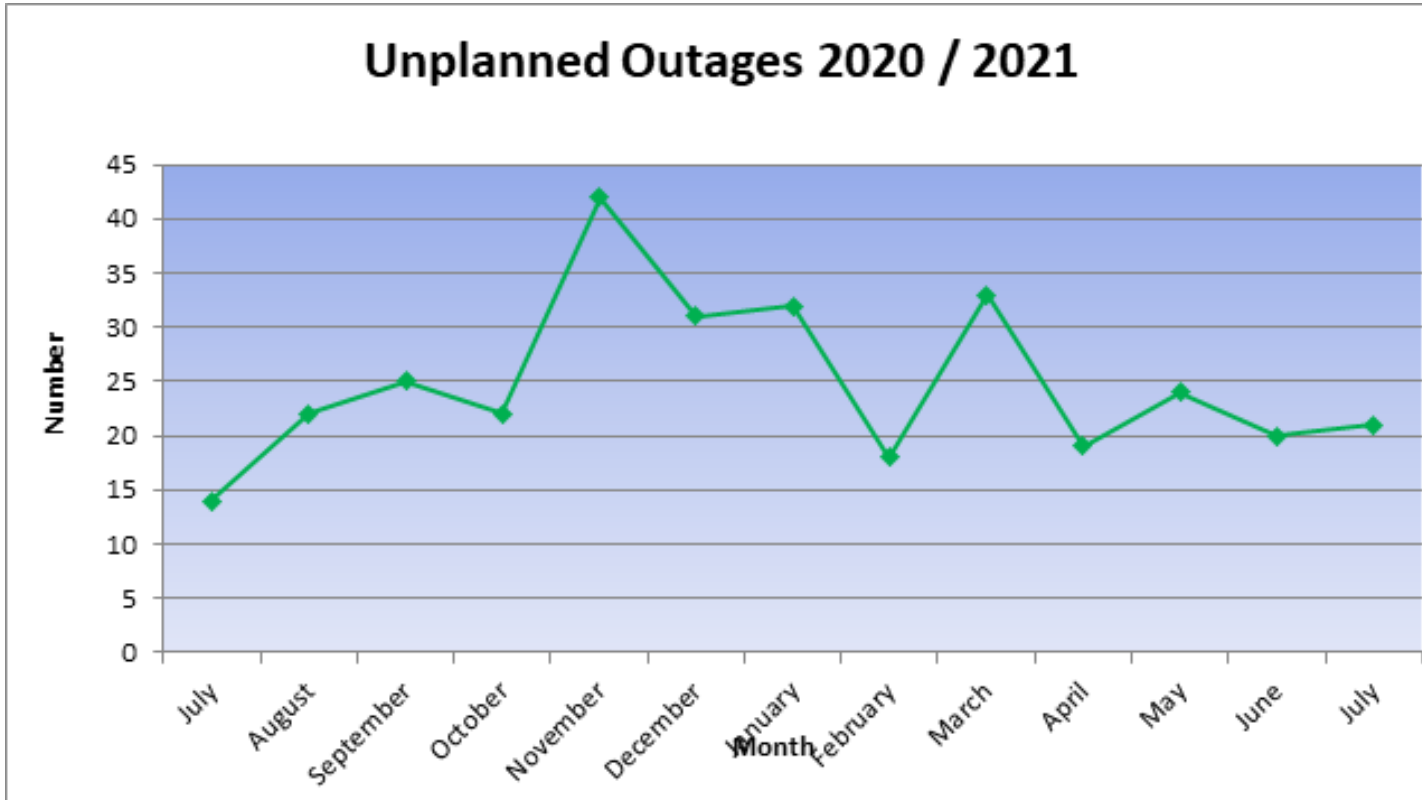

- Unplanned Outages – 22

Supplier	Unplanned Count
Supplier 1	3
Supplier 2	3
Supplier 3	3
Supplier 4	2
Supplier 5	2
Supplier 6	2
Supplier 7	2
Supplier 8	1
Supplier 9	1
Supplier 10	1
Supplier 11	1
HUB	1

- The HUB outage was due to a certificate issue with a supplier's EMMA

System Separation Project Update



Area	Jurisdiction	Task	Start	Finish	Status
Planning	Both	Market Participants to advise ReMCoDS of technical contacts	23 February 2021	23 February 2021	Complete
Planning	Both	High Level Market Plan issued to Market Participants	24 February 2021	24 February 2021	Complete
Design	NI	EMMA Technical Specification issued to NI (Dual Suppliers)	26 February 2021	26 February 2021	Complete
Planning	Both	Technical Questionnaire issued to Market Participants	26 February 2021	26 February 2021	Complete
Design	Both	Webforms Look and Feel Overview issued to Market Participants	05 March 2021	05 March 2021	Complete
Assurance	Both	Assurance Approach approved by RAs	09 April 2021	09 April 2021	Complete
Assurance	Both	Assurance Approach issued to Market Participants	12 April 2021	12 April 2021	Complete
Planning	NI	Deadline for Market Participants to have new NI EMMA infrastructure ready (To Be NI Production & NI Test)		30 April 2021	Complete
Planning	ROI	Market Participant's existing ROI Test EMMA Upgrades (some EMMA upgrades will be deferred until IPT Execution window)	29 April 2021	29 June 2021	Complete
Planning	NI	Market Participant's existing NI Test EMMA Upgrades (2 NI Only Suppliers)	29 April 2021	29 June 2021	Complete
Planning	NI	Market Participant's new NI Test EMMA Builds	05 May 2021	28 June 2021	Complete
Assurance	Both	Self-Assessment Participant Questionnaire issued	07 May 2021	07 May 2021	Complete
Assurance	Both	Return completed Participant Questionnaires to ReMCoDS	28 May 2021	28 May 2021	Complete
Assurance	Both	Assurance Bodies issue Self-Assessment Report to RAs	11 June 2021	11 June 2021	Complete
Assurance	Both	IPT Plan made available	21 June 2021	21 June 2021	Complete
Planning	NI	Market Participant's new NI Production EMMA Builds	28 June 2021	17 August 2021	Complete
Cutover	Both	High Level Cutover Approach issued to Market Participants	25 June 2021	25 June 2021	Complete
Assurance	Both	ESB Networks and NIE Networks Project Formal Assessment	05 July 2021	16 July 2021	Complete
Design	Both	Updated Webforms Guide issued to Market Participants	14 July 2021	14 July 2021	Complete
Assurance	Both	Assurance Bodies issue Formal Assessment Report to RAs	23 July 2021	23 July 2021	Complete
Assurance	Both	IPT Execution Window	09 August 2021	27 August 2021	In Progress
Cutover	Both	Detailed Cutover Plan issued to Market Participants	03 September 2021	03 September 2021	On Track
Assurance	Both	IPT and Final Exit Report issued to RAs	10 September 2021	10 September 2021	On Track
Cutover	Both	Hypercare Approach issued to Market Participants	15 September 2021	15 September 2021	On Track
Assurance	Both	CRU and UR final engagement	17 September 2021	17 September 2021	On Track
Cutover	Both	Execute Cutover	25 September 2021	26 September 2021	On Track
Cutover	Both	Hypercare Window	26 September 2021	04 November 2021	On Track
Cutover	ROI	Market Participant's ROI Production EMMA Upgrades	30 September 2021	22 October 2021	On Track

Issued 09 August 2021

- **Key Activities up to August 2021**
- Production and Test EMMA Builds completed
- IPT Plan issued to Market Participants
- IPT Workshop for NI Market Participants completed
- Webforms Installation and User Guides issued to Market Participants
- High level Cutover approach issued to Market Participants
- Project Formal Assessment Completed
- **Project Plan on Track – IPT Test Phase in Progress**

Webforms Installation Process

- Installation Guide and Pack issued on 09 August 2021
- A number of issues were encountered by various suppliers during self installation process
- Issues being reviewed and any learnings/improvements will be incorporated into the new installation pack ahead of cutover

System Separation Project Update



Project Activities up to October 2021

- IPT Testing to be completed
- Detailed Cutover Plan to be issued to Market Participants
- Final Market Assurance Report issued to RAs
- Cutover and Hypercare activities



An Coimisiún
um Rialáil Fóntas

Commission for
Regulation of Utilities

CRU SMART Metering Update 25.08.2021


AOB

Next Steps

Diary dates for next ReMCoWG meeting:

- **Wednesday 3rd November 2021 – Belfast (subject to change)**

Dates for 2021 are on Calendar of Events on RMDS website www.rmdservice.com

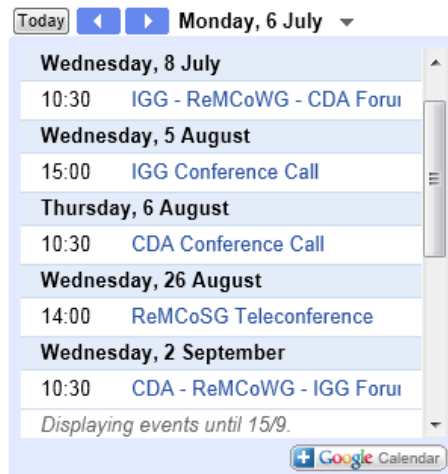

ReMCoDS

Retail Market Coordination Design Service

Thank You
